

2020 Census Program Management Review

2020 Census Schedule

Raphael Corrado
Decennial Directorate


April 8, 2015

Final v1.0

Outline

- Reengineered Schedule Tier Concept
- Tiers 1 and 2 Overview
- Updated 2020 Census Life Cycle Chart
- 2020 Census Schedule Management - What's Next

Reengineered Schedule Tier Concept (Notional)

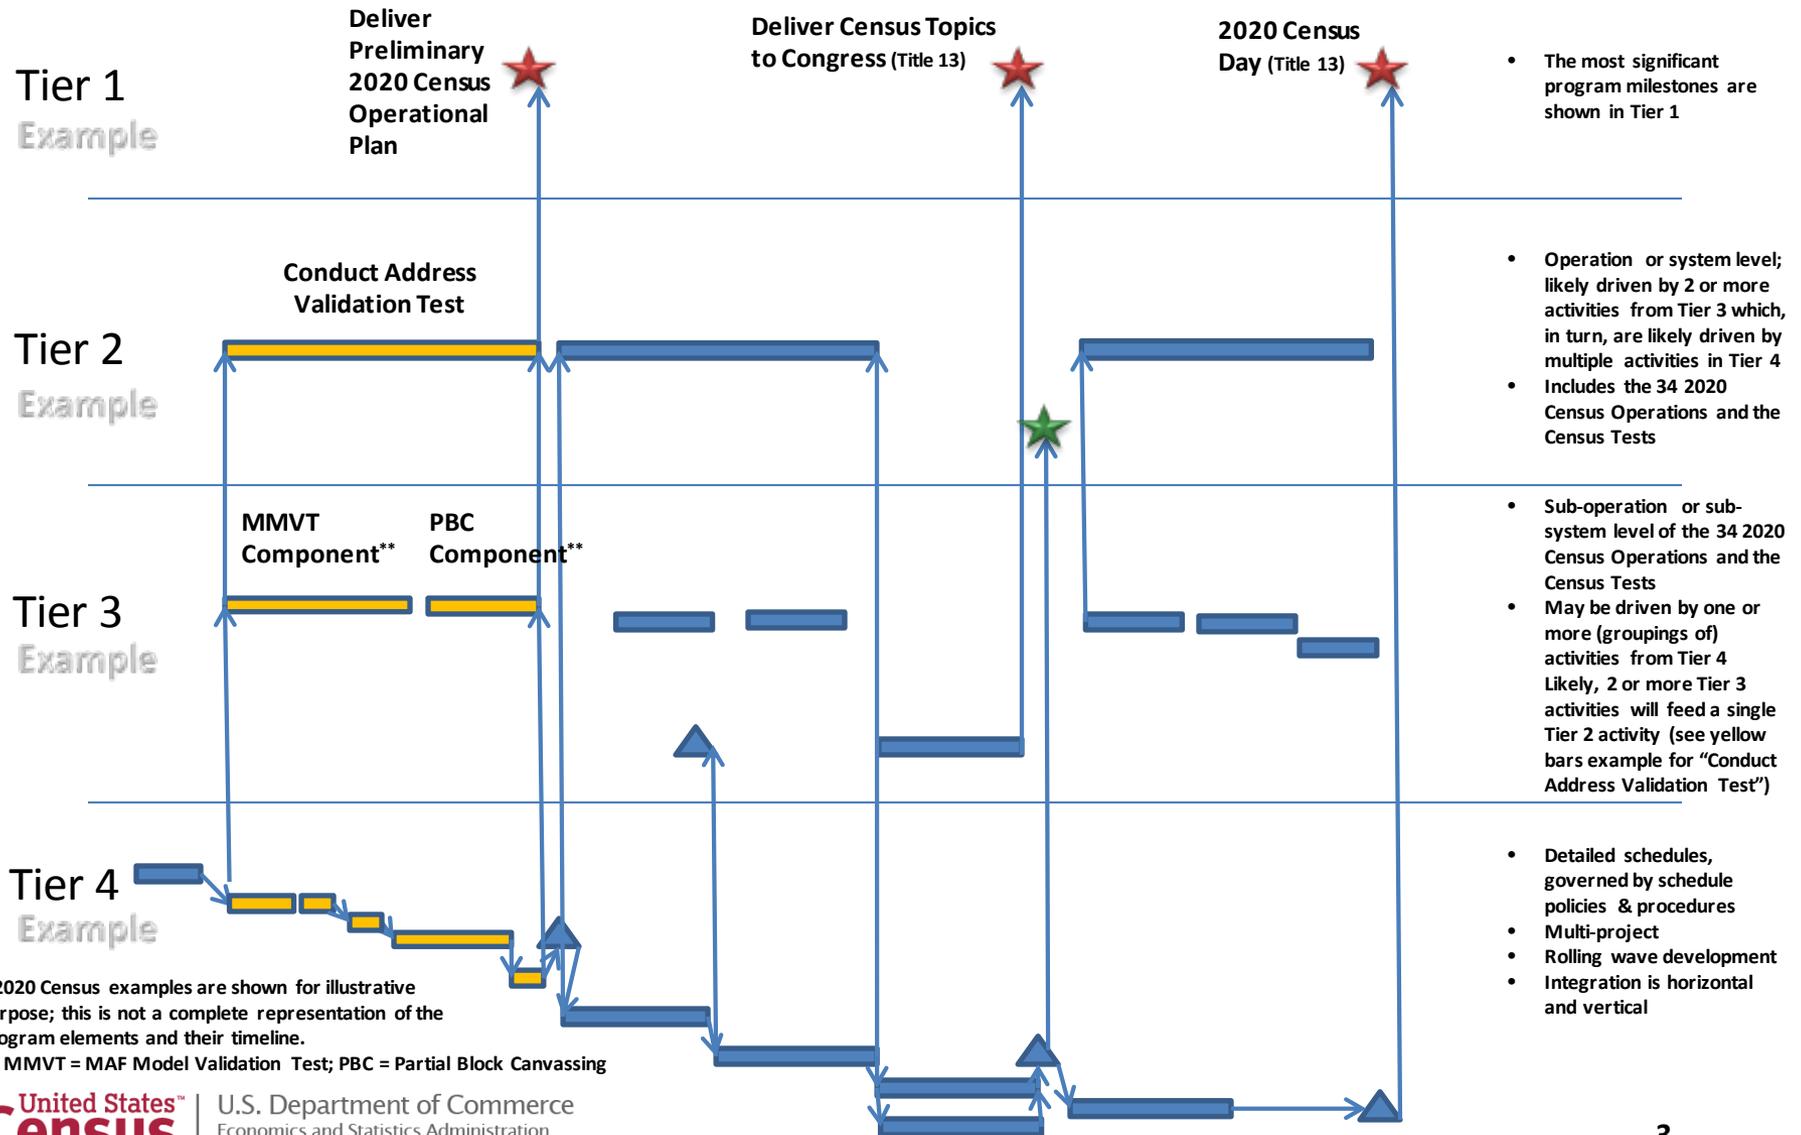

* 2020 Census examples are shown for illustrative purpose; this is not a complete representation of the program elements and their timeline.

** MMVT = MAF Model Validation Test; PBC = Partial Block Canvassing

Tier 1 - Program Milestones

PROGRAM LEVEL MILESTONES - TIER 1


Milestone	Date
Begin 2020 Census (Title 13)	11/18/2011
Deliver Preliminary 2020 Decennial Census Operational Plan	09/30/2015
Deliver 2020 Census Topics to Congress (Title 13)	04/01/2017
Deliver 2020 Census Questions to Congress (Title 13)	04/01/2018
Deliver 2020 Decennial Census Operational Plan	09/28/2018
Complete Local Update of Census Addresses (LUCA) Program (including Appeals Process) (P.L.103-430)	09/30/2018
2020 Census Day (Title 13)	04/01/2020
Deliver Apportionment Counts to the President (U.S.C. Article 1, Section 2)	12/31/2020
Complete Delivery of Redistricting Counts to the States (P.L.94-171)	03/31/2021
Complete 2020 Census (Title 13)	09/29/2023

Tier 2 - Program Master Schedule


- Includes the 34 2020 Census Operations and all Census Tests
- Spans the 2020 Census Life Cycle
- Further decomposed into Tier 3 (sub-operations and sub-systems) and Tier 4 (detailed, team level) Schedules

20PC \$ 02.01 Program Management	
20PCS-354.05	Perform Program Management Functions (Budget, Schedule, Risk, Performance Measurement)
20PCS-354.20	Implement Strategic Communications
20PCS-370.20	Finalize Internal Review of Tier 1 and 2 Activities
20PCS-370.30	Finalize Descriptions of Tier 3 and 4 Activities
20PCS-370.40	Create Resource Loaded Schedules Launched using the Enterprise WBS
20PC \$ 02.02 Census/Survey Engineering	
20PCS-351.50	Conduct Languages Services
20PCS-352.00	Conduct Content and Forms Design
20PCS-370.60	Conduct Coverage Improvement
20PCS-354.10	Implement Security, Privacy, and Confidentiality
20PCS-354.30	Implement Legal and Policy Support
20PC \$ 02.03 Frame	
20PCS-351.50	Conduct Local Update of Census Addresses (LUCA)
20PCS-351.40	Conduct Geographic Programs
20PCS-351.60	Conduct Address Canvassing
20PCS-351.70	Conduct Update Enumerate
20PC \$ 02.05 Response Data	
20PCS-352.70	Conduct Nonresponse Followup
20PCS-352.30	Conduct Internet Self Response
20PCS-352.40	Conduct Non-ID Processing
20PCS-352.10	Conduct Paper Processing
20PCS-352.90	Conduct Census Questionnaire Assistance
20PCS-352.80	Conduct Overseas Enumeration Program
20PCS-352.50	Conduct Group Quarters Operations
20PCS-350.90	Conduct the Island Areas Program
20PCS-352.20	Conduct Communications
20PCS-352.60	Conduct Enumeration at Transitory Locations
20PCS-353.10	Conduct Count Review
20PCS-353.00	Conduct Response Processing
20PC \$ 02.06 Published Data	
20PCS-353.50	Conduct the Redistricting Data Program
20PCS-353.40	Conduct Archiving Activities
20PCS-353.30	Conduct Count Question Resolution Process
20PCS-353.20	Disseminate Data Products
20PC \$ 02.07 Test and Evaluation	
20PCS-304.10	Conduct the National Census Contact Test
20PCS-303.10	Conduct 2013 Census Test (Data Collection Period)
20PCS-303.30	Conduct 2014 Census Test
20PCS-303.95	Conduct 2015 Address Validation Test
20PCS-370.70	Conduct 2014 Simulated Exercise (SIMEX)
20PCS-304.00	Conduct 2015 Census and Optimizing Self Response Tests
20PCS-304.15	Conduct 2015 National Content Test
20PCS-354.45	Conduct 2015 Simulated Exercise (SIMEX)
20PCS-351.00	Conduct Coverage Measurement Program
20PCS-370.00	Conduct 2030 Research and Planning
20PCS-370.10	Conduct Evaluations
20PCS-354.40	Conduct 2016 Census Test
20PCS-354.50	Conduct 2016 Address Canvassing Test
20PCS-354.60	Conduct 2017 Census Test
20PCS-307.80	Conduct Operational Readiness Test
20PCS-187.90	Complete Release Post Enumeration Survey Results
20PCS-188.00	Complete Release Evaluation and Experimentation Reports
20PC \$ 02.08 Infrastructure	
20PCS-353.90	Establish Field Infrastructure
20PCS-370.50	IT Infrastructure - Non-Census Enterprise Data Collection and Processing (Non-CEDCaP)
20PCS-354.00	IT Infrastructure - Census Enterprise Data Collection and Processing (CEDCaP)
20PCS-353.80	Service Center

2020 Census Life Cycle Chart – Operational Development and Systems Testing

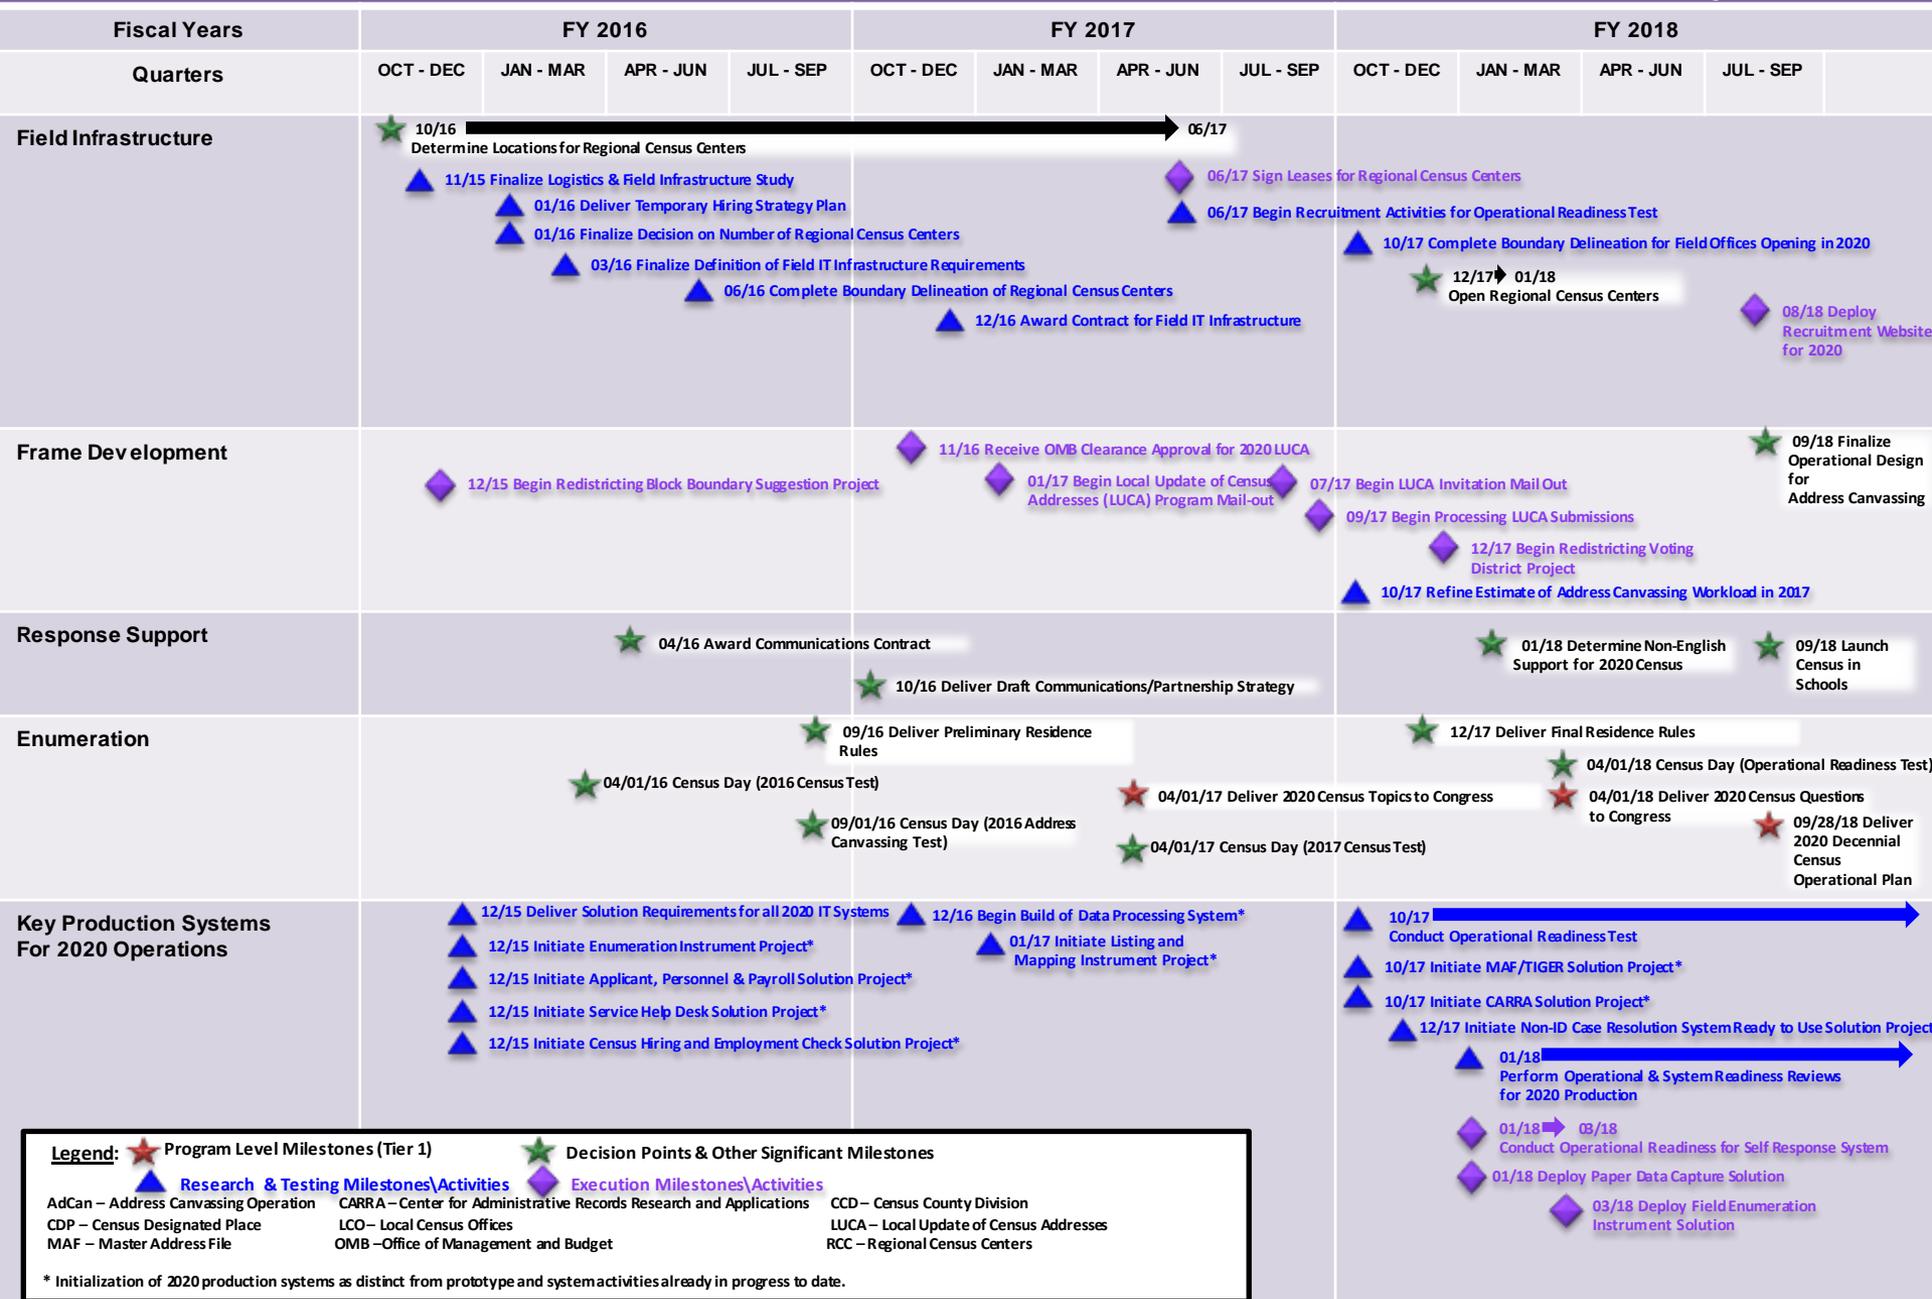

2020 Census Life Cycle Chart – Implementation

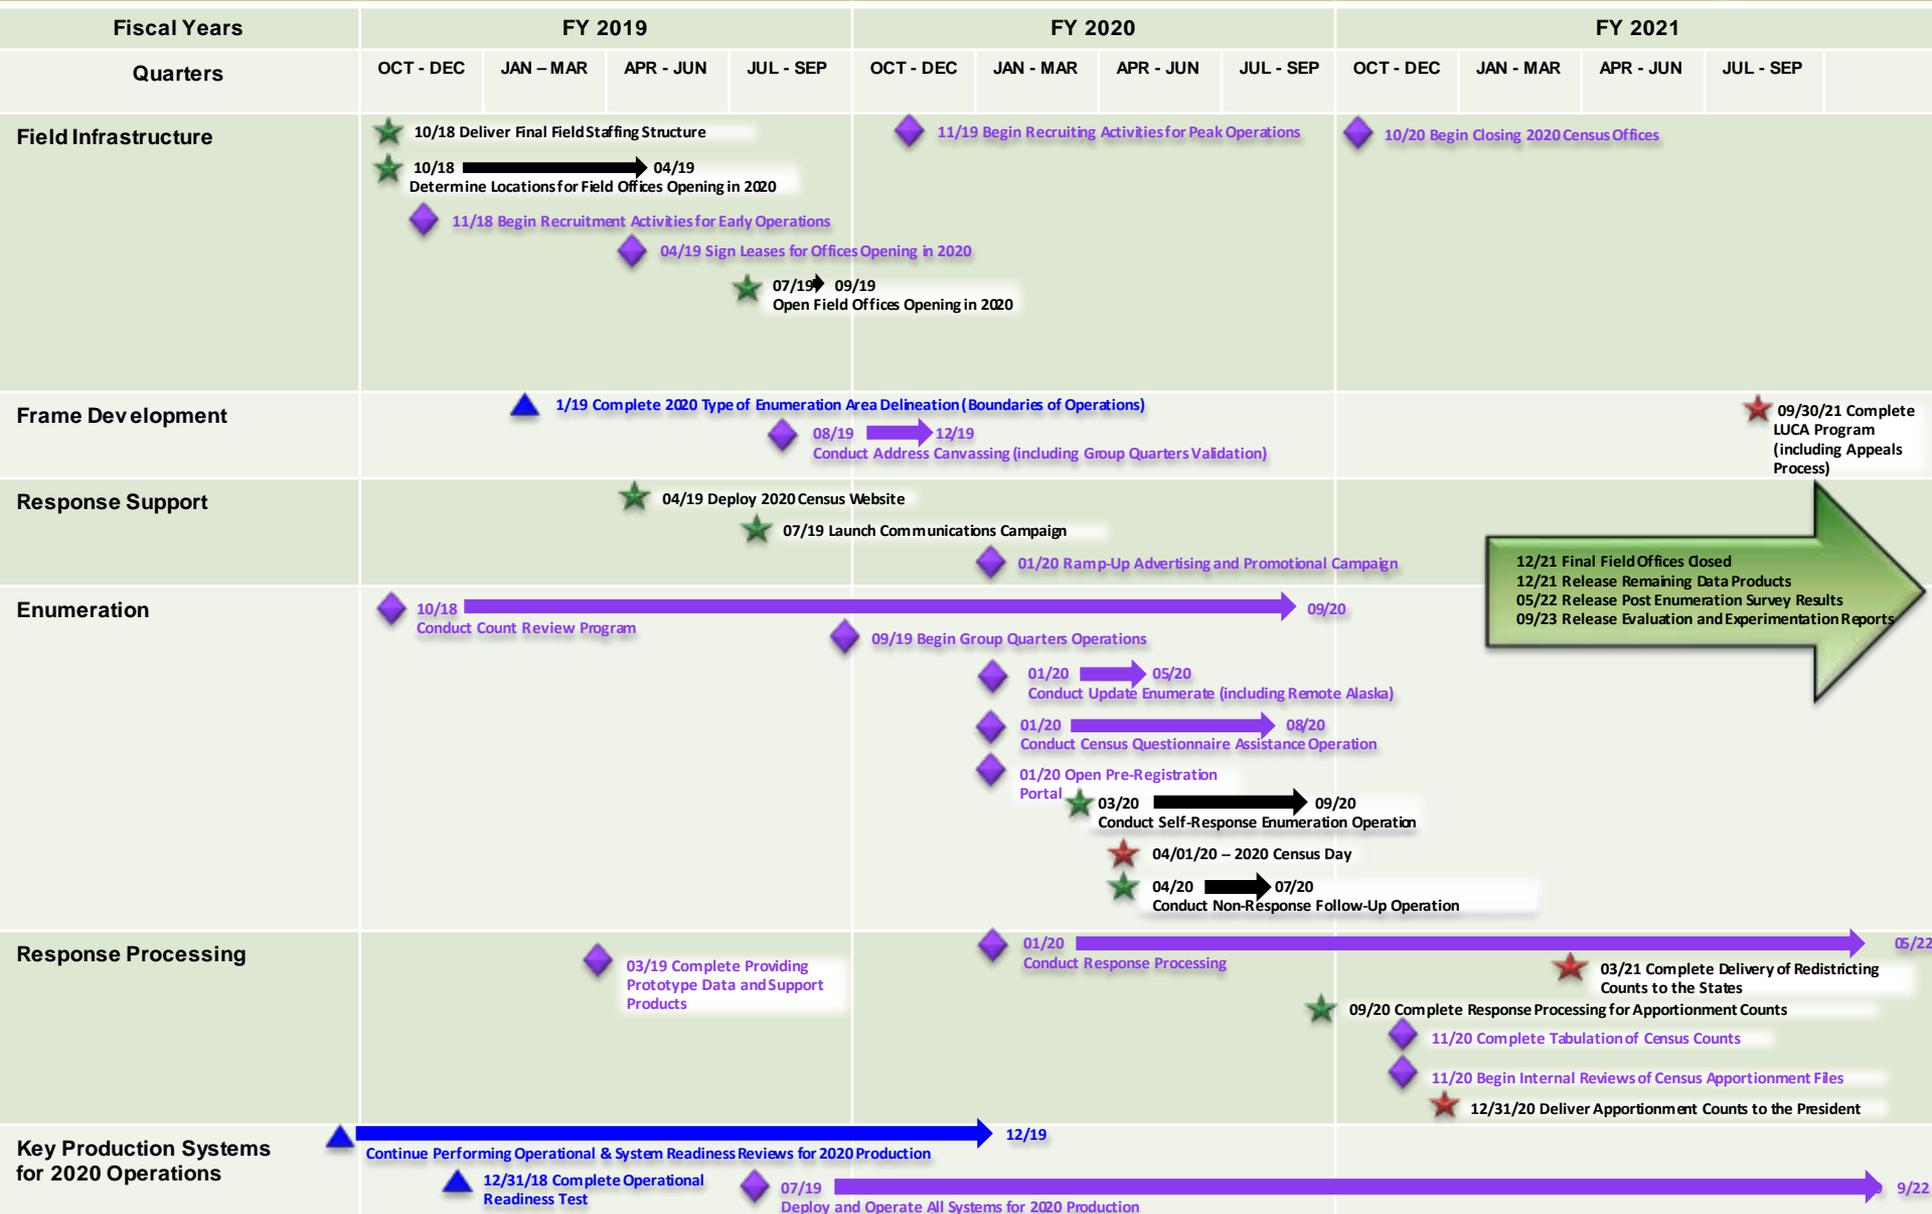

12/21 Final Field Offices Closed
12/21 Release Remaining Data Products
05/22 Release Post Enumeration Survey Results
09/23 Release Evaluation and Experimentation Reports

Legend:

- ★ Program Level Milestones (Tier 1)
- ▲ Research & Testing Milestones/Activities
- ◆ Execution Milestones/Activities
- ★ Decision Points & Other Significant Milestones/Activities

Source: U.S. Census Bureau 2020 Census Research & Planning Office

2020 Census Schedule Management

What's Next

- Continue refining Tier 3 schedules as we complete the Preliminary 2020 Census Decennial Operational Plan
- Continue developing integrated Tier 4 schedules for the upcoming Census Tests and the 2020 Census Operations
- Embedding professional scheduling staff into each 2020 Census team to optimize detailed schedules development and control
- Continuous schedule monitoring and statusing on a weekly basis

Thank You

- Send questions to the email address below.

census.2020.program.management.review@census.gov
